




# Data Center Power Upgrade: Current Status



Steel Grate Removals from Equipment Yard for Chiller #4

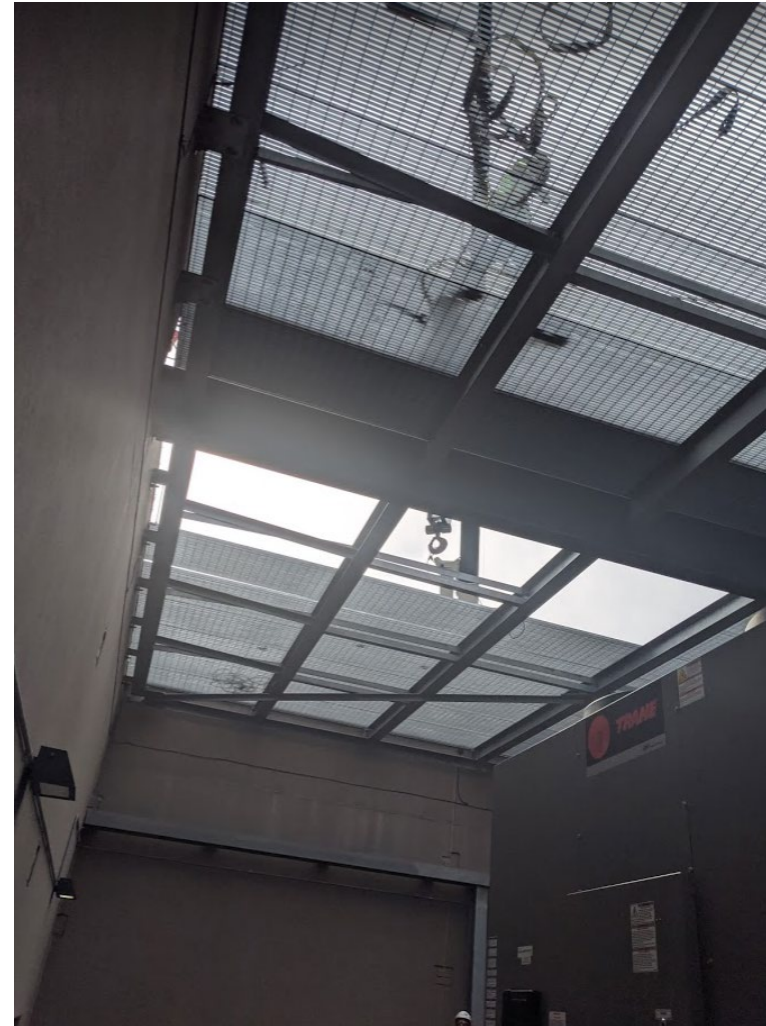



# Data Center Power Upgrade: Current Status



Contamination Partition in Data Hall 2





# HiPerGator AI

UNIVERSITY OF FLORIDA





# HiPerGator 3.0 Current Status



# Consolidated Timeline

Status Update Date	10/9/2020																		Completion Status
Project Activities	2020												2021						Completion Status
	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sept	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	
Project Kickoff	█																		100%
Engagement with Construction & Engineering Firms	Scope, Design, Constructability, Procurement Review																		100%
Prepare and Execute Early Release Packages For Long Lead Items			Facilities Design Review & Finalize																100%
Construction Mobilization								General Contractor Oversight											28%
Mechanical Plant								Chillers Delivery & Install											22%
Electrical Plant								Utility & Switch Gear Delivery & Install											20%
Telecommunication								IT Network Integrations Installation and Testing											15%
HiPerGator 3.0 Invitation To Negotiate		Initiate, Review and Finalize ITN																	100%
HiPerGator 3.0 Negotiate and Place Order																			100%
HiPerGator 3.0										Delivery, Setup & Startup									1%
HiPerGator 3.0 Project Closeout																			0%
HiPerGator AI-NVIDIA		Finalize HiPerGator AI Cluster Design, Bill of Material & Procurement																	100%
HiPerGator AI										Delivery, Setup & Startup									2%
HiPerGator AI Project Closeout																			0%
Redundant Generator Installation																Delivery, Setup & Startup			0%
Miscellaneous Commissioning Activities									Load & Configuration Testing										10%
UFDC Power Upgrade Project Closeout																			0%



# Consolidated Timeline

